

Springfield Union Station

Project Update - July 2015

Work Completed and Underway


- Completed Pressure Injected Footings for the Parking Garage
- Continuing masonry repairs inside and outside the Terminal Building
- Completed installing the aggregate piers in the Busway
- Completed the chipping of the aggregate piers to the proper elevation
- Completed removal of the known underground storage tank
- Completed removal of the formerly unknown and ruptured underground storage tank




7/15 - The exposed PIFs stand like the Chinese Terracotta Warriors but these will soon be chipped down to become the warriors that will hold up the parking garage.



7/15 - Activity by the mason contractor behind the Terminal Building.

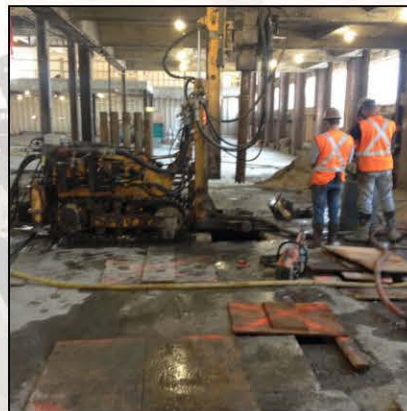

7/15 - Here are the micro-piles being installed inside the Terminal Building to support the new elevators in three locations.

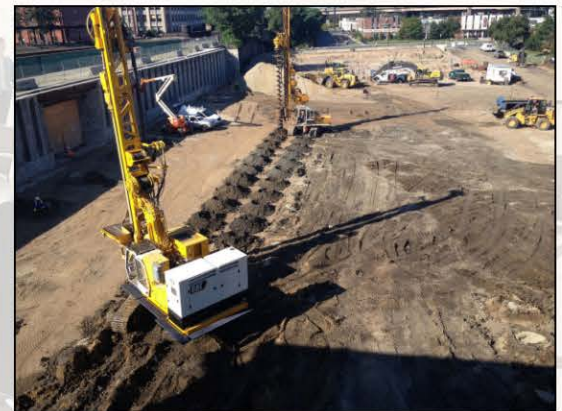

7/15 - Watching the two machines makes one think of the old game "whack-a-mole", where one drills the hole and the other fills it. This will be accomplished over 500 times in the Busway. Further away, the site of the parking garage can also be seen.

Upcoming Work

- Installation of forms for cast in place (CIP) pile caps to start in early August with concrete placement to follow
- New electric vault construction to begin in early August
- Continued masonry work both inside and outside the Terminal Building
- Installation of storm drainage in Liberty Street Connector
- Subgrade preparation and utility installation in Busway
- Sewer line and water line installation in Frank B. Murray Street
