

Springfield Union Station

Project Update - November 2014

Work Completed and Underway


- Finished abatement of Terminal Building roof
- Installed temporary roof waterproofing
- Completed preparations for demolition of former baggage building
- Began total demolition of former baggage building



11/2014 As part of preparation for demolition, the canopy has been removed from the former baggage building. Along with other interior demolition, its attachment to the Terminal building was severed.



11/2014 The old asbestos laden Terminal Building roof has been removed and a liquid waterproofing applied to protect the building during the winter months.

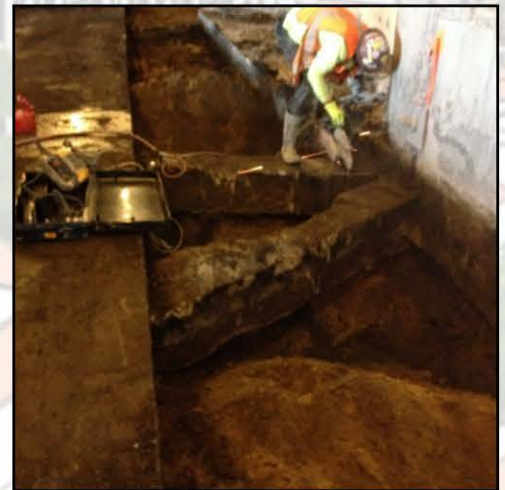

11/2014 The last step in preparation for the demolition of the former baggage building was the cutting of the grade beam ties to the retaining wall for the rail lines.

Upcoming Work

- Removal of parapets and corbel stones anchored to roof to prevent them from falling
- Continue selective interior demolition of Terminal Building
- Begin soil nailing in locations that will become accessible once former baggage building is demolished
